APEX CURTAINS

INSTALLATION PACK

Ready for a beautiful finish.

Alex & Morgan Taylor (fictional clients) ·
The Garden House
12 Example Lane
Sample Village
Illustrative address only
Appointment: To be confirmed

Confirm access arrangements with the customer.

Pack and check

- [ ] Drill
- [ ] Suitable drill bits
- [ ] Electric screwdriver and driver bits
- [ ] Charged batteries and charger
- [ ] Ladders or specified access equipment
- [ ] Saw suitable for cutting tracks
- [ ] Tape measure and level
- [ ] Detector where required
- [ ] Protective equipment and floor covers
- [ ] Clean-up equipment
- [ ] Tracks labelled by room and window
- [ ] Track components, brackets, gliders and end stops
- [ ] Screws and suitable fixings
- [ ] Curtains labelled by room, window and panel
- [ ] Tiebacks in the correct colour and quantity
- [ ] Hooks or holdbacks in the correct finish
- [ ] Operation tested at every window
- [ ] Finished length and tieback positions checked
- [ ] Customer shown how to operate the curtains
- [ ] Aftercare explained and brochure provided
- [ ] Outstanding issues recorded
- [ ] Installation complete

Care at handover

Show the customer how to operate the track, release tiebacks and gently dress the folds. Explain Dry clean only, the gentle dust-removal routine, and the complete care guide in their brochure. Refer cleaning, persistent creases or changes in the hang to Apex before treatment or adjustment.

APEX · PANEL LABELS B287B2CE

Drawing room
Garden apex

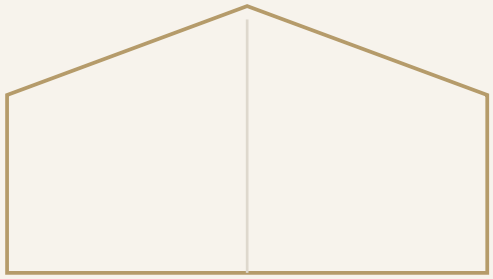

Two-sided apex · shape guide only · use the recorded site dimensions

TRACK AND OPENING

Forest Group CS® Contract System · White · Centre opening

DIMENSIONS

Two-sided apex; width 3200 mm; left 2400 mm; middle 3600 mm; right 2400 mm; longest 3600 mm. Left slant 2000 mm; right slant 2000 mm; peak 1600 mm from left. Calculated from the entered dimensions, rounded to the nearest mm.

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Warm flax · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Warm flax; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____

STANDARD · PANEL LABELS D3E54284

Principal bedroom
Main window

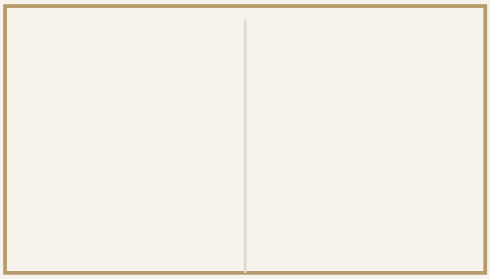

Standard window · shape guide only · use the recorded site dimensions

TRACK AND OPENING

Forest Group KS® Klick System · White · Centre opening

DIMENSIONS

2200 mm width; 2600 mm finished drop. Horizontal track.

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Soft sage · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Soft sage; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____
