APEX CURTAINS

INSTALLATION PACK

Ready for a beautiful finish.

Alex & Morgan Taylor (fictional clients) ·
The Garden House
12 Example Lane
Sample Village
Illustrative address only
Appointment: To be confirmed

Confirm access arrangements with the customer.

Pack and check

- [ ] Drill
- [ ] Suitable drill bits
- [ ] Electric screwdriver and driver bits
- [ ] Charged batteries and charger
- [ ] Ladders or specified access equipment
- [ ] Saw suitable for cutting tracks
- [ ] Tape measure and level
- [ ] Detector where required
- [ ] Protective equipment and floor covers
- [ ] Clean-up equipment
- [ ] Tracks labelled by room and window
- [ ] Track components, brackets, gliders and end stops
- [ ] Screws and suitable fixings
- [ ] Curtains labelled by room, window and panel
- [ ] Tiebacks in the correct colour and quantity
- [ ] Hooks or holdbacks in the correct finish
- [ ] Operation tested at every window
- [ ] Finished length and tieback positions checked
- [ ] Customer shown how to operate the curtains
- [ ] Aftercare explained and brochure provided
- [ ] Outstanding issues recorded
- [ ] Installation complete

Care at handover

Show the customer how to operate the track, release tiebacks and gently dress the folds. Explain Dry clean only, the gentle dust-removal routine, and the complete care guide in their brochure. Reassure them about normal settling, handling creases, texture variations and edge light. Demonstrate simple checks for an occasional catch and emphasise regular care, clear tracks and gentle operation without forcing the curtain.

APEX · PANEL LABELS B287B2CE

Drawing room
Garden apex

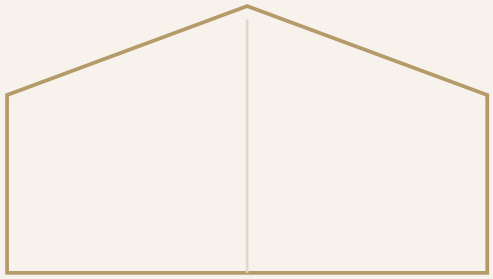

Two-sided apex · shape guide only · use the recorded site dimensions

TRACK AND OPENING

Forest Group CS® Contract System · White · Centre opening

DIMENSIONS

Two-sided apex; width 3200 mm; left 2400 mm; middle 3600 mm; right 2400 mm; longest 3600 mm. Left slant 2000 mm; right slant 2000 mm; peak 1600 mm from left. Calculated from the entered dimensions, rounded to the nearest mm.

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Warm flax · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Warm flax; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____

STANDARD · PANEL LABELS D3E54284

Principal bedroom
Main window

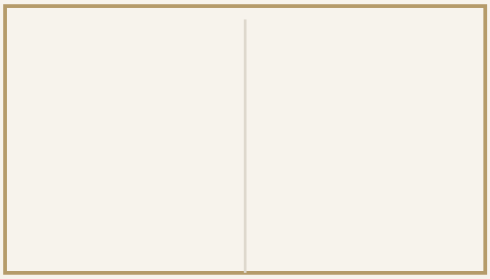

Standard window · shape guide only · use the recorded site dimensions

TRACK AND OPENING

Forest Group KS® Klick System · White · Centre opening

DIMENSIONS

2200 mm width; 2600 mm finished drop. Horizontal track.

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Soft sage · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Soft sage; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____
