APEX CURTAINS

INSTALLATION PACK

Ready for a beautiful finish.

Alex & Morgan Taylor (fictional clients) ·
The Garden House
12 Example Lane
Sample Village
Illustrative address only
Appointment: To be confirmed

Confirm access arrangements with the customer.

Pack and check

- [ ] Drill
- [ ] Suitable drill bits
- [ ] Electric screwdriver and driver bits
- [ ] Charged batteries and charger
- [ ] Ladders or specified access equipment
- [ ] Saw suitable for cutting tracks
- [ ] Tape measure and level
- [ ] Detector where required
- [ ] Protective equipment and floor covers
- [ ] Clean-up equipment
- [ ] Tracks labelled by room and window
- [ ] Track components, brackets, gliders and end stops
- [ ] Screws and suitable fixings
- [ ] Curtains labelled by room, window and panel
- [ ] Tiebacks in the correct colour and quantity
- [ ] Hooks or holdbacks in the correct finish
- [ ] Operation tested at every window
- [ ] Finished length and tieback positions checked
- [ ] Customer shown how to operate the curtains
- [ ] Aftercare explained and brochure provided
- [ ] Outstanding issues recorded
- [ ] Installation complete

APEX CURTAINS

APEX · PANEL LABELS B287B2CE

Drawing room
Garden apex

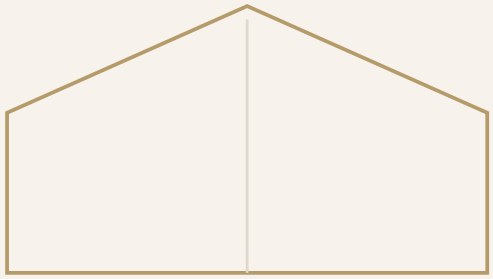

Shape guide only · use the recorded site dimensions

TRACK AND OPENING

Made-to-measure apex track · Warm white · Centre opening

DIMENSIONS

3200 mm coverage; longest 3600 mm; left/right drops 2400/2400 mm; apex offset 1600 mm; slopes 2000/2000 mm

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Warm flax · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Warm flax; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____

APEX CURTAINS

STANDARD · PANEL LABELS D3E54284

Principal bedroom
Main window

Shape guide only · use the recorded site dimensions

TRACK AND OPENING

Forest Group KS® Klick System · Matt white · Centre opening

DIMENSIONS

2200 mm coverage; longest 2600 mm

ACCESS AND FIXINGS

3800 mm working height; track height confirm onsite mm; To be confirmed onsite

CURTAINS

Textured linen · Soft sage · 2 panel(s) · Double pinch pleat

FINISH

Touching the floor

TIEBACKS AND HOOKS

2 × Matching fabric Soft sage; 2 × Classic holdback Bronze

Window instructions

Confirm final mounting and fitting details onsite.

Fitter checks: packed _____ installed _____ operation checked _____
Outstanding details _____
